

Grant / Project Name	Grantor	Treatment Funds Awarded*	Activities/ Treatments to date	Remaining Treatment Funds*	Status	Exp Date
<b>North Susanville WUI Fuels Treatments</b>	CALFIRE	\$2,999,924.32	CEQA cleared. Landowner agreements complete. Biomass 100% complete. Mastication 60% complete.	\$1,500,125	Biomass complete. Mastication will return Spring 2026 to finish Eagle Lake road FB. Arch surveys and hand thinning spring 2026. Hazard tree assessments ongoing. RFP for hand thinning, hazard tree, and arc surveys early 2026.	3/15/2030
<b>South Lassen Wildfire Recovery Project</b>	CALFIRE	\$6,469,424.33	Agreement executed. CEQA cleared. Pre-ops surveys completed. 2025 planting complete. Mechanical Site Prep Biomass 100% Complete. Mechanical Site Prep Mastication - 50% Complete. Reforestation activities - 15 % complete.	\$3,576,229.00	Winter weather will likely shut down ops. Site prep and reforestation to resume in Spring. 2026 resource specialist surveys spring 2026.	3/31/2030
<b>LFSC LNF Dixie Fire Hazard Tree Project</b>	CALFIRE	\$2,999,987.85	Agreement signed by LFSC. NEPA and CEQA complete. RFP for implementation closed on 1/14/2026	\$2,999,988	USFS agreement work, implementation in 2026.	3/15/2030
<b>Lassen County Wide Assessment</b>	SNC	\$275,242.00	Agreement executed 7/2024. Draft agreement received.	\$35,300	Review, comments, final assessment in early 2026.	10/31/2027

\* Does not include cost match information

Project	Grantor	Treatment Funds Awarded*	Activities/ Treatments to date	Remaining Treatment Funds*	Status	Exp. Date
Honey Lake Valley RCD/LFSC - SPA	NA	NA	MOU - SPA between organizations to assist HLRCD with biomass utilization, site prep, and tree planting. Biomass utilization complete on several landowners. Tree planting complete on several landowners.	NA	Winter period mechanical site prep active in Doyle and Janesville.	NA
Cradle Valley Site Prep	USFS	\$270,360.00	Mechanical site prep 100% complete.	\$32,998	Reforestation activities scheduled for 2026.	11/1/2026
Dyer Initiative WUI Fuels Treatments Phase II	CALFIRE	\$949,951.52	Signed agreement 1/20/2026	\$949,951.52	Collaborate with PCFSC on RFP for implementation early 2026	3/15/2029
Lassen Countywide Defensible Space Program	CALFIRE	\$949,999.43	Signed agreement 1/20/2026	\$949,999.43	Landowner signups open. RFPs for implementation early 2026	3/15/2029
Lyonsville Fuelbreak (TGU)	CALFIRE	948,209.43	Signed agreement 1/20/2026	948,209.43	RFPs for implementation early 2026	3/15/2029
Shingletown Phase 2 Community Treatments (SHU)	CALFIRE	949,924.89	Signed agreement 1/20/2026	949,924.89	Landowner signups open. RFPs for implementation early 2026	3/15/2029
Shingletown Phase 2 Fuelbreaks (SHU)	CALFIRE	\$949,473.25	Signed agreement 1/20/2026	\$949,473	RFPs for implementation early 2026	3/15/2029
Lassen County Coordinator	CA Fire Safe Council	138,493.00	firewise, cwpp, local/ regional partnerships	25,521.54	final deliverables	7/1/2026

\* Does not include cost match information

Project	Grantor	Treatment Funds Awarded*	Activities/ Treatments to date	Remaining Treatment Funds*	Status	Exp. Date
<b>Eastside Communities SPA #018 / Lone Spring SNC #1275</b>	USFS/SNC	1,291,202	Completed EA, resource specialist surveys in Lonespring completed.	\$343,026.00	Continued surveys for implementation 2026-2027. Implementation prioritization.	3/31/2031
<b>TPI Data Collection</b>	USDA - RAC	82,815	Agreement executed 7/2024.	82,815	Identifying priority areas to survey.	9/21/2027
<b>Susanville WUI Planning</b>	USDA - RAC	46,750	Tentative award,	46,750	working on final agreement. Identifying priority survey needs.	

\* Does not include cost match information

Grant / Project Name	Grantor	Treatment Funds Awarded*	Activities/ Treatments to date	Remaining Treatment Funds*	Status	Exp Date
<b>Bootsole-SNC #1305</b>	SNC	\$3,671,725.00	NEPA, resource specialist surveys, layout, cruising, + 2,820 acres of implementation: 1,899 acres mechanical thinning, 562 acres hand thinning, 359 acres mechanical fuels	\$0	Completed	1/1/2026
<b>Diamond Mountain - SNC #1065</b>	SNC	\$882,087.00	896 acres of treatment: Plantation thinning - 130 ac, Aspen hand treatments - 57 ac, hand chipping - 133 acres, pile burning - 476 acres	\$0	Completed	1/1/2026
<b>USFS Cradle Valley / Bootsole Dixie Fire Salvage</b>	USFS	2,600,000	1,609 acres completed: Cobbler thinning: 888 acres, Bootsole Salvage: 506 acres, Cradle Valley Salvage 215	\$0	Completed	3/15/2029

##


\* Does not include cost match information

Planned / Proposed Projects 1/20/2026

Project	Treatment Cost	Grantor / Program	Planned Project	Status
Shingletown Phase II - Manton	2,000,000	TBD	CEQA complete. Priority Phase 2 treatments in manton area deinated.	Not funded in 2025. Will re-aply with MFSC partnership.
Cow Creek Forest and Watershed Restoration Project.	\$6,500,000	TBD	landscape level fuels reduction and forest health treatments in area between communities of Whitmore and Shingletown.	WSRCD is CEQA lead. 24/25 FH grant unsuccessful, will resubmit in 26.
South Susanville WUI Treatments	TBD	TBD	Dead/ Dying/ Hazard Tree removal, biomass fuels treatments, mastication.	Approached by several landowners about separate projects. LFSC would like to combine into a larger landscape level project. CEQA CLEARANCE Planned 2026. RAC funded planning. Likely a 26 WP grant or prop 4 app.
Eastside Communities: Lone Spring Project - Phase 1	4,500,000	TBD	Hazardous fuels reduction/ FOREST HEALTH in Lonespring project area of Eastside Communities project	Arch surveys and Wildlife surveys completed for lonespring area in 2024. 24/25 FH grant unsuccessful, can resubmit in 26.
Big Valley Mountain Phase II	TBD	TBD	Work with CALFIRE and large landowners to identify next areas of treatment.	Project delineation and CEQA clearence to commence in 2026. 2026 WP grant
Dyer Mountain Phase II / East Shore Project	TBD	TBD	Priority Phase 2 treatments deinated and funded. More funding needed to keep project progressing south towards PCFSC project, which is working north.	Likely a 2026 grant app.
Thompson Peak Initiative Phase II	TBD	TBD	Work with landowners and agency partners to identify priority landscape level fuels reduction areas in WUI. Janesville, Milford, Doyle potential community treatments.	Potential project meetings ongoing. Engaging potential project partners. CEQA clearance completed for Phase I project. Likely a 26 WP application
Acer Forest Health - ELP priority	TBD	TBD	landscape level fuels reduction and forest health treatments in area west of Eagle Lake. - ELP Priority Project	24/25 FH grant unsuccessful, can likely resubmit in 26.
Dixie South Lassen - Public Lands	TBD	TBD	Dixie Recovery project in WUI and WUI adjacent. - ELP Priority Project	ELP project list
LNF/PNF Cross Boundary - Diamonds	TBD	TBD	LMU Priority project - followup Rx under burning in previously completed mechanical units. Cross forests, districts, and counties.	ELP project list

County Line  
★ Active  
● Planning

1/21/2026  
LFSC General Meeting  
Project Update

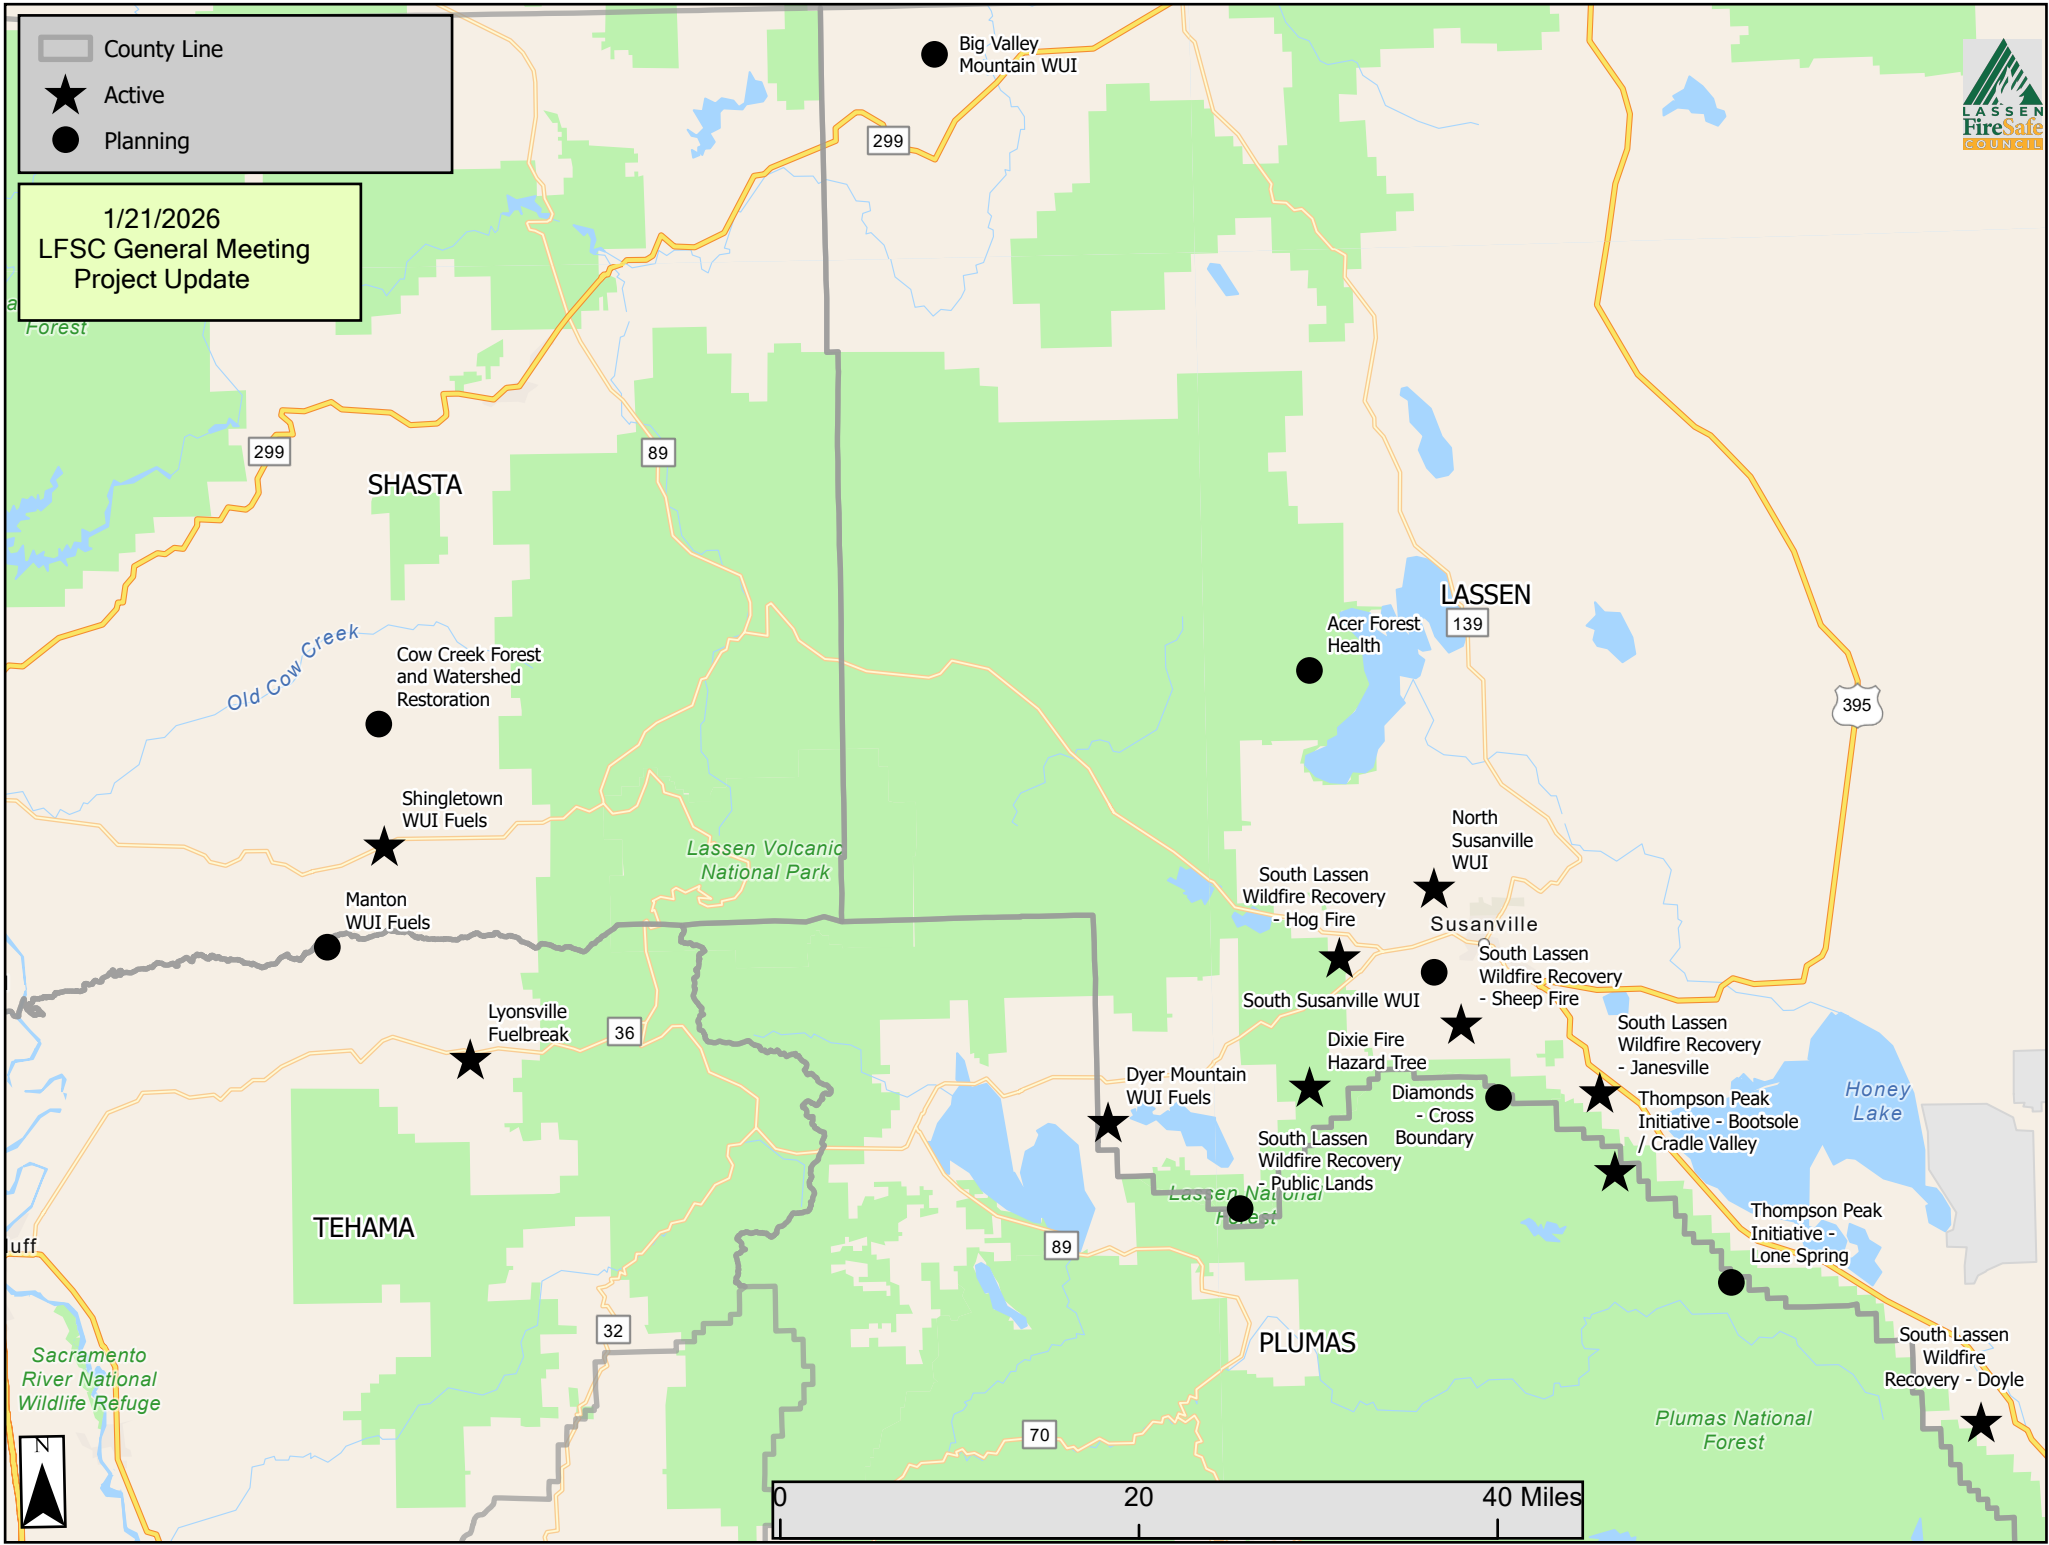

● Big Valley Mountain WUI

SHASTA

LASSEN

TEHAMA

PLUMAS

Old Cow Creek

Cow Creek Forest and Watershed Restoration

Acer Forest Health

★ Shingletown WUI Fuels

● Manton WUI Fuels

★ Lyonsville Fuelbreak

★ South Lassen Wildfire Recovery - Hog Fire

★ North Susanville WUI

★ South Susanville WUI

● South Lassen Wildfire Recovery - Sheep Fire

★ South Lassen Wildfire Recovery - Janesville

★ Dixie Fire Hazard Tree

● Diamonds - Cross Boundary

★ Thompson Peak Initiative - Bootsole / Cradle Valley

★ Dyer Mountain WUI Fuels

● South Lassen Wildfire Recovery - Public Lands

● Thompson Peak Initiative - Lone Spring

Sacramento River National Wildlife Refuge

Plumas National Forest

★ South Lassen Wildfire Recovery - Doyle

